



सिद्धार्थनगर नगरपालिका
नगर कार्यपालिकाको कार्यालय
सिद्धार्थनगर, रुपन्देही
लुम्बिनी प्रदेश, नेपाल

आ.व. २०७९।८० को वार्षिक प्रगति समीक्षा

प्रस्तुतकर्ता: साकार श्रेष्ठ
इन्जिनियर, सिद्धार्थनगर नगरपालिका
मिति :- २०८०/०५/१०, आइतबार

1

प्रस्तुतिको विषय सूची (Content of Presentation)

- १) ठेक्का प्रक्रियाको विवरण (निर्माण सम्बन्धि)
- २) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding – NCB) विवरण (निर्माण सम्बन्धि)
- ३) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को दरभाउपत्रको (Sealed Quotation- SQ) विवरण (निर्माण सम्बन्धि)
- ४) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. मा राष्ट्रिय बोलपत्र मार्फत भएका कामहरु मध्ये केहि मुख्य मुख्य कामहरु (निर्माण सम्बन्धि)
- ५) सिद्धार्थनगर नगरपालिकाबाट संचालित बहुबर्षिय योजना
- ६) कार्यक्रम कार्यान्वयनमा देखिएका समस्याहरू
- ७) महत्वपूर्ण कार्यहरुको फोटोहरु
- ८) अनुगमनका फोटोहरु

2

1

१) ठेक्का प्रक्रियाको विवरण (निर्माण सम्बन्धि)					
प्रकार	रकम	सूचना म्याद कम्तिमा	मुल्यांकन समय	आशय समय	सम्भावित समय
कोटेशन (Direct Purchase)	९,९९,९९९ सम्म	३ - ७ दिन	३ - ७ दिन	-	३ - ७ दिन
दरभाउ पत्र (Sealed Quotation- SQ)	१० लाख देखि १९,९९,९९९ सम्म	१५ दिन	७ दिन	सूचना दिईने	७ दिन
राष्ट्रिय बोलपत्र (National Competitive Bidding - NCB)	२० लाख माथि	३० दिन	७ दिन	७ दिन	१५ दिन

3

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
1	NCB/SNP/01/079-080 (e-bid)	Building Construction Work, Shree Paklihuwa Secondary School, Ward no. - 01	विशेष अनुदान (संघीय)	1	20,000,000.00	2079-05-29 (16th October, 2022)	श्री अभियन्ता कन्स्ट्रक्सन, प्रा.लि., वुटवल-९	13,212,866.17	-33.94%	2079.08.13	2080.02.15	8,211,392.30	Running
2	NCB/SNP/02/079-080 (e-bid)	Construction and Upgrading of Road and Drain works at West side Darkhasuwa passing through Siddhartha Yatayat Samiti, Ward no. - 03	नगर स्तरीय	3	5,999,849.12	2079-05-29 (16th October, 2022)	श्री वैष्णवी निर्माण सेवा, बगहा-२	4,526,559.90	-24.56%	2079.08.21	2080.01.05	4,056,152.41	Complete
3	NCB/SNP/03/079-080	Construction of Road, Drain and other structures including building maintenance and plumbing on different locations of Ward no. 12	वडा स्तरीय	12	4,698,528.68	2079-06-05 (21 September, 2022)	श्री अहमद निर्माण सेवा, सि.न.पा.-९	3,750,442.26	-20.18%	2079.08.15	2080.01.07	3,570,829.94	Complete
4	SNP/NCB-04/079-080	Basdiliya Surya path ra Lumbini road dekhri footsal hudai BP path jodne sadak tatha nala nirman, RCC Road Construction work at Bihani path, Construction of Drain at Laliguras path, Basdila, Ward 8	नगर स्तरीय	8	4,298,399.21	2079-06-13 (29 September, 2022)	श्री विशाल निर्माण सेवा, मायादेवी-७	3,120,897.00	-27.39%	2079.08.13	2080.01.07	3,120,701.24	Complete
5	SNP/NCB-05/079-080	Construction of Road and Drain Work at ward 5	वडा स्तरीय	5	2,073,758.69	2079-06-13 (29 September, 2022)	श्री विशाल निर्माण सेवा, मायादेवी-७	1,616,965.45	-22.03%	2079.08.12	2080.01.07	1,419,662.00	Complete
6	SNP/NCB-06/079-080	RCC Road & Drain Construction Work, Drain and Road Construction Work, One Side Drain and Road Construction Work, Road PCC Construction Work, Road PCC Construction Work, One Side Drain and Road Construction Work & PCC Road Construction Work, Ward 8	वडा स्तरीय	8	4,181,913.06	2079-06-13 (29 September, 2022)	श्री मोहम्मद राजी निर्माण सेवा, सियारी-४	3,260,641.16	-22.03%	2079.08.13	2080.01.07	3,086,628.97	Complete

4

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
7	SNP/NCB-07/079/080	Construction of Road and Drain Work at ward 7	बडा स्तरीय र अन्य पूँजीगत	7	3,491,423.28	2079-06-13 (29 September, 2022)	श्री शितला निर्माण सेवा, सि.न.पा.-९	2,672,453.24	-23.46%	2079.08.12	2080.01.07	2,618,755.16	Complete
8	SNP/NCB-08/079/080	Fulpur Culvert, Fulpur Remain Road and Drain work, Jhandi Bazar to dadagaun at ward No. 2, Siddharthanagar Municipality	बडा स्तरीय	2	3,849,999.49	2079-06-14 (30 September, 2022)	श्री क्रान्ति निर्माण सेवा, सि.न.पा.-२	3,765,386.94	-2.20%	2079.08.14	2080.01.07	3,729,209.05	Complete
9	SNP/NCB-09/079/080	Drain & Road Construction work at Kul Shrestha Ghar road, Jhuma Subedi and rajesh Bishwakarma Ghar to upto pauwa hotel, way to Ajmullaha house, way to pipariya hanuman baniya house at ward No. 6, Siddharthanagar Municipality	बडा स्तरीय	6	5,294,008.29	2079-06-14 (30 September, 2022)	श्री शितला निर्माण सेवा, सि.न.पा.-९	4,092,633.91	-22.69%	2079.08.25	2080.01.08	3,811,449.63	Complete
10	SNP/NCB-10/079/080	Construction of Surya dev ma.vi School Building at ward No. 10 Siddharthanagar Municipality	नगर स्तरीय र अन्य पूँजीगत	10	5,068,186.79	2079-06-14 (30 September, 2022)	श्री एमआरएम कन्स्ट्रक्सन, बुटवल-७	3,402,487.13	-32.87%	2079.08.13	2080.01.30	2,955,878.22	Complete
11	SNP/NCB-11/079/080	Construction of RCC road Works at ward no. 9, Siddharthanagar Municipality	नगर स्तरीय	9	2,995,959.48	2079-06-14 (30 September, 2022)	श्री ओमसाई कन्स्ट्रक्सन, बसन्तपुर-४	2,174,762.05	-27.41%	2079.08.13	2080.01.30	2,096,119.56	Complete
12	SNP/NCB-12/079/080	Construction of Road, Drain and other Structures on Different Locations of ward no. 13,	बडा स्तरीय	13	2,951,353.67	2079-06-14 (30 September, 2022)	श्री मोहम्मद राजी निर्माण सेवा, सियारी-४	2,430,321.75	-17.65%	2079.08.25	2080.01.08	2,209,170.28	Complete
												5	

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
13	SNP/NCB-13/079/080	Construction of Road, Drain and other Structures on Different Locations of ward no. 03,	बडा स्तरीय	3	5,321,696.71	2079-06-14 (30 September, 2022)	श्री मानिष निर्माण सेवा, सि.न.पा.-८	3,861,805.29	-27.43%	2079.08.26	2080.01.07	3,385,643.28	Complete
14	SNP/NCB-14/079/080 (e-bid)	Construction of Shree Nawadurga Secondary School Building at SNP Ward no. - 04	विशेष अनुदान (संघीय)	4	19,938,849.29	2079-06-14 (30 September, 2022)	श्री जगरनाथ निर्माण व्यवसाय, तिलोत्तमा-५	13,251,914.81	-33.54%	2079.09.19	2080.02.15	13,172,892.71	Complete
15	SNP/NCB-15/079/080	Ward Office Building Construction Work at Siddharthanagar Municipality, Ward no. 7	नगर स्तरीय र अन्य पूँजीगत	7	5,231,744.78	2079-06-25 (11 October, 2022)	श्री अहमद निर्माण सेवा, सि.न.पा.-९	5,103,081.44	-2.46%	2079.08.13	2080.01.31	4,946,782.32	Complete
16	SNP/NCB-16/079/080	Construction and fixing of drain slab at Si.Na.Pa.-08, Durga Mandir	नगर स्तरीय	8	2,997,420.68	2079-07-01 (18 October, 2022)	श्री एस.एस. निर्माण सेवा, सि.न.पा.-११	2,910,602.41	-2.90%	2079.08.27	2080.02.30	2,894,490.01	Complete
17	SNP/NCB-17/079/080	Drain & RCC Road Construction Work, Ward No. 1	बडा स्तरीय	1	3,002,285.34	2079-07-04 (21 October, 2022)	श्री एस.एस. निर्माण सेवा, सि.न.पा.-११	2,926,874.11	-2.51%	2079.08.29	2080.02.30	2,885,028.32	Complete
18	SNP/NCB-18/079/080	Construction of Ward Office Building Works, Ward No. 2	नगर स्तरीय	2	3,890,699.23	2079-07-04 (21 October, 2022)	श्री क्रान्ति निर्माण सेवा, सि.न.पा.-२	3,794,072.00	-2.48%	2079.09.18	2080.03.03	3,423,516.51	Complete
												6	

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
19	SNP/NCB-19/079/080	Construction of Guard House Building and Remaining Boundary wall at Panch Batika (Prithivi Park), Ward No. 2	नगर स्तरीय	2	2,999,999.61	2079-07-04 (21 October, 2022)	श्री क्रान्ति निर्माण सेवा, सि.न.पा.-२	2,920,694.00	-2.64%	2079.09.18	2080.03.03	2,754,772.75	Complete
20	SNP/NCB-20/079/080	Construction of Road and Drain Works (Ward No. 10)	वडा स्तरीय	10	3,348,105.36	2079-07-06 (23 October, 2022)	श्री अन्जुली कन्स्ट्रक्सन, सि.न.पा.-६	2,613,730.00	-21.93%	2079.09.25	2080.01.18	2,375,051.30	Complete
21	SNP/NCB-21/079/080 (e-bid)	Construction of Guard Room, Drain, Footpath and Upgrading Compound wall and Landscaping at Darkhasuwa Park, Ward No. 3	समपुरक अनुदान र नगर स्तरीय	3	9,999,882.83	2079-07-20 (06 November, 2022)	श्री बागेश्वरी निर्माण सेवा, सि.न.पा.-१०	7,471,079.40	-25.29%	2079.09.25	2080.02.31	6,434,851.70	Complete
22	SNP/NCB-22/079/080	Construction and upgrading of Road, Drain and other structures on different locations of Ward No. 11	वडा स्तरीय	11	4,497,970.20	2079-07-21 (07 November, 2022)	श्री सफिक निर्माण सेवा, सि.न.पा.-११	4,384,933.00	-2.51%	2079.10.03	2080.02.30	3,875,087.71	Complete
23	SNP/NCB-23/079/080	Construction Work for Black Top Road on Brihaspati and Prakritik path of Ward No. 9	शशर्त अनुदान (संघीय) र अन्य पूँजीगत	9	2,779,075.10	2079-07-22 (08 November, 2022)	श्री मन्जुल कन्स्ट्रक्सन प्रा.लि., सि.न.पा.-९	2,716,393.26	-2.26%	2079.09.28	2080.02.30	2,616,115.93	Complete
24	SNP/NCB-24/079/080	Construction of Road and Drain Works on different locations of Ward No. 9	वडा स्तरीय	9	3,549,312.70	2079-07-22 (08 November, 2022)	श्री मानिप निर्माण सेवा, सि.न.पा.-८	3,459,547.61	-2.53%	2079.09.22	2080.02.30	2,577,180.60	Running

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
25	SNP/NCB-25/079/080	Construction of RCC Road and Drain Works on different locations of Ward No. 9	वडा स्तरीय र अन्य पूँजीगत	9	3,865,567.89	2079-07-22 (08 November, 2022)	श्री मोहम्मद गाजी निर्माण सेवा, सियारी-४	3,773,870.67	-2.37%	2079.10.03	2080.02.30	3,742,848.23	Complete
26	SNP/NCB-26/079/080	Construction of Khajana Basic School, Ward No. 3	नगर स्तरीय	3	3,276,346.63	2079-07-22 (08 November, 2022)	श्री प्रितम विन्डर्स, सि.न.पा.-४	3,195,356.09	-2.47%	2079.10.03	2080.02.30	2,012,513.98	Complete
27	SNP/NCB-27/079/080	Drain and Road Construction Work, Siddharthanagar-1, Radhakrishna path Naudihawa	वडा स्तरीय र अन्य पूँजीगत	1	2,729,948.88	2079-07-23 (09 November, 2022)	श्री शितला निर्माण सेवा, सि.न.पा.-९	2,664,913.45	-2.38%	2079.10.03	2080.02.30	2,664,302.58	Complete
28	SNP/NCB-28/079/080	Construction of Road, Drain and other structures on different locations of Ward No. 8	वडा स्तरीय	8	2,577,406.17	2079-07-30 (16 November, 2022)	श्री सौरभ विन्डर्स, सि.न.पा.-६	2,118,954.00	-17.79%	2079.09.26	2080.03.01	2,056,584.08	Complete
29	SNP/NCB-29/079/080	Construction of Mandabya Sewa Samaj Briddashram of Ward No. 9	शशर्त अनुदान (संघीय) र अन्य पूँजीगत	9	3,230,665.90	2079-07-30 (16 November, 2022)	श्री प्रितम विन्डर्स, सि.न.पा.-४	2,445,044.66	-24.32%	2079.09.28	2080.03.01	2,260,529.74	Complete
30	SNP/NCB-30/079/080	Construction of Road, Drain and other structures on different locations of Ward No. 4	नगर स्तरीय	4	4,899,789.70	2079-07-30 (16 November, 2022)	श्री सौरभ विन्डर्स, सि.न.पा.-६	4,122,852.81	-15.86%	2079.09.26	2080.03.01	2,148,098.79	Running

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
31	SNP/NCB-31/079/080 (e-bid)	Building Construction Work of Bahira Baal Ma. Bi. Ward No. 2	शशर्त अनुदान (संघीय) र अन्य पूँजीगत	2	7,003,478.87	2079-08-21 (7 December, 2022)	श्री वैष्णवी निर्माण सेवा, बगाहा-२	5,107,292.38	-27.07%	2079.11.16	2080.03.12	4,856,954.38	Complete
32	SNP/NCB-32/079/080	Drain and Road Construction Work at Ward No. 6 (Package 2)	बडा स्तरीय र अन्य पूँजीगत	6	3,334,351.20	2079-08-21 (7 December, 2022)	श्री अहमद निर्माण सेवा, सि.न.पा.-९	2,627,175.63	-21.21%	2079.10.26	2080.02.30	2,373,669.08	Complete
33	SNP/NCB-33/079/080	Drain and RCC Road Construction Work, Siddharthanagar Municipality-7, Vijaya Path & Ramjanaki Path, Rupandehi	शशर्त अनुदान (प्रदेश) र अन्य पूँजीगत	7	4,082,425.17	2079-08-29 (15 December, 2022)	श्री शितला निर्माण सेवा, सि.न.पा.-९	3,128,826.22	-23.36%	2079.11.04	2080.03.09	3,125,103.59	Complete
34	SNP/NCB-34/079/080	Construction of Boundary wall at Shree Nawadurga Secondary School, Ward No. 4	विशेष अनुदान (संघीय)	4	5,030,101.63	2079-08-29 (15 December, 2022)	श्री भिमगंगा निर्माण सेवा, सि.न.पा.-८	3,342,113.64	-33.56%	2079.11.04	2080.03.09	3,034,962.74	Complete
35	SNP/NCB-35/079/080	Construction of Road, Drain and other structures on different locations of Ward No. 11	नगर स्तरीय	11	2,699,068.06	2079-08-29 (15 December, 2022)	श्री पाल कन्स्ट्रक्सन, काठमाडौं-१०	1,941,214.63	-28.08%	2079.11.04	2080.03.09	1,905,721.26	Complete
36	SNP/NCB-36/079/080	Construction of Drain and Road at Karma Path to up to Education Mandir (Somai Mai Path), Durga Colony to East Road of Ward No. 6	नगर स्तरीय र विभिन्न ठेक्काबाट बचत रकम	6	2,780,045.93	2079-09-01 (16 December, 2022)	श्री शितला निर्माण सेवा, सि.न.पा.-९	2,030,848.68	-26.95%	2079.11.08	2080.03.09	1,920,106.96	Complete
												9	

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
37	SNP/NCB-37/079/080 (e-bid)	Construction of Parking Area (Interlock Paving), Meeting Hall shed, wastage collection shed at Bhim Hospital of Ward No. 13	नगर स्तरीय	13	7,999,746.47	2079-09-01 (16 December, 2022)	श्री शर्मा निर्माण सेवा, चापपानी-६, पाल्पा	5,960,572.64	-25.49%	2079.11.10	2080.03.12	1,237,174.22	Running
38	SNP/NCB-38/079/080 (e-bid)	Building Construction Work (Shree Mahatma Gautam Buddha Secondary School) at Ward No. 06	विशेष अनुदान (संघीय)	6	19,999,702.67	2079-09-03 (18 December, 2022)	श्री शैलेश निर्माण सेवा, सि.न.पा.-६	14,111,253.39	-29.44%	2079.11.08	2080.03.20	13,316,662.71	Running
39	SNP/NCB-39/079/080 (e-bid)	Playground Infrastructure Construction Works, Ward No. 03	नेपाल सरकार नगद अनुदान	3	9,999,534.24	2079-09-08 (23 December, 2022)	श्री विशाल निर्माण सेवा, मायादेवी-७	6,108,339.04	-38.91%	2079.11.16	2080.03.04	6,075,584.13	Complete
40	SNP/NCB-40/079/080 (e-bid)	Construction of Garage for Tractors and other vehicles of Siddharthanagar Municipality at Bus Park of Ward No. 3	नेपाल सरकार नगद अनुदान	3	7,493,382.61	2079-09-13 (28 December, 2022)	श्री अनुराधा कन्स्ट्रक्सन, सि.न.पा.-९	6,157,631.34	-17.83%	2079.11.04	2080.03.05	5,812,802.84	Complete
41	SNP/NCB-41/079/080	Construction of Toilet at Balmandir, Khajahana School and Bhujauli School, Ward No. 3, 5 & 11	नगर स्तरीय र नेपाल सरकार नगद अनुदान	3, 5, 11	5,826,002.15	2079-09-22 (6 January, 2023)	श्री लक्ष्मी निर्माण सेवा, सि.न.पा.-१३	4,627,283.16	-20.58%	2079.11.28	2080.02.20	3,203,046.14	Running
42	SNP/NCB-42/079/080	Construction of Drain, Drain Cover & RCC Road Construction Work at Siddharthanagar Municipality, Ward No. 7	बडा स्तरीय	7	2,823,457.14	2079-09-30 (14 January, 2023)	श्री कोटहीमाई कन्स्ट्रक्सन	2,150,760.73	-23.83%	2079.11.28	2080.02.32	1,976,438.23	Complete
												10	

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
43	SNP/NCB-43/079/080	Construction of Dharmashala Building Construction Work at Siddharthanagar Municipality, Ward No. 10	वडा स्तरीय	10	4,676,905.33	2079-10-04 (18 January, 2023)	श्री मोहम्मद गाजी निर्माण सेवा, सियारी-४	3,324,453.58	-28.92%	2079.12.10	2080.02.32	3,164,106.75	Complete
44	SNP/NCB-44/079/080 (e-bid)	Construction of Susanskrit Ma. Vi. Building Works inside Susanskrit School Boundary, Ward No. 13	नगर स्तरीय र शशर्त अनुदान (संधीय)	13	10,830,889.57	2079-10-12 (26 January, 2023)	श्री प्रितम विल्डर्स, सि.न.पा.-४	7,569,163.48	-30.12%	2079.12.24	2080.03.10	5,466,469.07	Running
45	SNP/NCB-45/079/080 (e-bid)	Building Construction Work of Bhanu Ma. Bi., Ward No. 9	रास्ट्रपति शैक्षिक सुधार कार्यक्रम	9	2,248,144.85	2079-10-05 (17 February, 2023)	श्री शितला निर्माण सेवा, सि.न.पा.-९	2,191,385.90	-2.52%	2079.12.27	2080.03.10	2,020,919.96	Complete
46	SNP/NCB-46/079/080	Road Maintenance work at Siddharthanagar Municipality, Ward No. 1 & 7	नगर स्तरीय र सडक बोर्ड नेपाल	1, 7	3,609,726.87	2079-11-30 (14 March 2023)	श्री ओमसाई कन्स्ट्रक्सन, वसन्तपुर-४	3,521,934.02	-2.43%	2080.01.25	2080.03.15	3,340,282.20	Complete
47	SNP/NCB-47/079/080	Road Maintenance work at Siddharthanagar Municipality, Ward No. 5, 9, 12 & 13	नगर स्तरीय र सडक बोर्ड नेपाल	5, 9, 12, 13	5,203,520.90	2079-11-30 (14 March 2023)	श्री अहमद निर्माण सेवा, सि.न.पा.-९	5,057,467.56	-2.81%	2080.01.24	2080.03.15	5,036,085.16	Complete
48	SNP/NCB-48/079/080	Road Maintenance work at Siddharthanagar Municipality, Ward No. 4, 8 & 11	नगर स्तरीय र सडक बोर्ड नेपाल	4, 8, 11	3,993,089.03	2079-11-30 (14 March 2023)	श्री राज कन्स्ट्रक्सन, सि.न.पा.-८	3,866,291.85	-3.18%	2080.01.27	2080.03.15	3,839,454.12	Complete
												11	

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
49	SNP/NCB-49/079/080	Road Maintenance work at Siddharthanagar Municipality, Ward No. 2 & 6	नगर स्तरीय र सडक बोर्ड नेपाल	2, 6	4,023,907.33	2079-11-30 (14 March 2023)	श्री सफिक निर्माण सेवा, सि.न.पा.-११	3,901,798.99	-3.03%	2080.01.25	2080.03.15	3,843,563.04	Complete
50	SNP/NCB-50/079/080	Road Maintenance work at Siddharthanagar Municipality, Ward No. 3 & 10	नगर स्तरीय र सडक बोर्ड नेपाल	3, 10	3,381,746.57	2079-11-30 (14 March 2023)	श्री लक्ष्मी निर्माण सेवा, सि.न.पा.-१३	3,305,479.65	-2.26%	2080.01.25	2080.03.15	3,212,342.65	Complete
51	SNP/NCB-51/079/080	Road Construction work at Satsanga Path Ward No. 06	अन्य पूँजीगत	6	4,566,163.99	2079-12-15 (29 March 2023)	श्री वैष्णवी निर्माण सेवा, बगाहा-२	3,283,035.54	-28.10%		2080.03.15	2,944,377.65	Complete
52	SNP/NCB-52/079/080	Chhath Pokhari Construction Work, Siddharthanagar-1, Naudihawa	अन्य पूँजीगत	1	3,421,435.21	2079-11-12 (24 February, 2023)	श्री अन्जुली कन्स्ट्रक्सन, सि.न.पा.-६	3,331,671.18	-2.62%	2079.12.30	2080.03.15	2,181,476.59	Running
53	SNP/NCB-53/079/080	Drain Repairing and Road Construction Work, Ward No. 3	नगर स्तरीय र लागत सहभागिता	3	4,025,491.66	2079-11-18 (2 March, 2023)	श्री सफिक निर्माण सेवा, सि.न.पा.-११	3,226,716.12	-19.84%	2080.01.14	2080.03.10	2,821,395.13	Complete
54	SNP/NCB-54/079/080	Construction of RCC Road Work at Ward No. 10	नगर स्तरीय र लागत सहभागिता	10	2,391,351.58	2079-11-18 (2 March, 2023)	श्री शितला निर्माण सेवा, सि.न.पा.-९	1,996,924.06	-16.49%	2080.01.17	2080.03.10	1,960,766.32	Complete
												12	

२) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को राष्ट्रिय बोलपत्रको (National Competitive Bidding - NCB) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
55	SNP/NCB-55/079/080	The Supply and Delivery of Fibre Desk and Bench	विशेष अनुदान (सघीय)	1	4,340,787.42	2079-12-16 (30 March, 2023)	श्री एम.एस.टि. फर्निचर उद्योग, सि.न.पा.-४	4,339,290.40	-0.03%	2080.02.16	2080.03.15	4,339,290.40	Complete
56	SNP/NCB-56/079/080	Construction of Finishing Work of Community Agriculture Market Infrastructure Development (Block A) at Ward No. 5	नगर स्तरीय र समपुरक अनुदान	5	18,123,236.94	2079-12-21 (4 April, 2023)	श्री कुशल निर्माण सेवा, अर्घाखाँची	12,018,070.57	-33.69%	2080.02.11	2080.03.15	9,103,956.13	Complete
					306,947,840.15			239,989,130.35	-21.81%			209,224,950.75	

कुल लागत = ३०,६९,४७,८४०.९५

कुल ठेक्का कबोल रकम = २३,९९,८९,९३०.३५

कुल ठेक्का घटी % = २१.८१ %

13

३) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को दरभाउपत्रको (Sealed Quotation- SQ) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
1	SNP/SQ/01/079-080	Construction and Upgrading of Drain Works (Samyak Path), Ward No. 3	नगर स्तरीय	3	1,799,732.99	2079-07-06	श्री सफिक निर्माण सेवा, सि.न.पा.-११	1,379,552.00	-23.35%	2079.09.03	2080.01.17	1,298,209.49	Complete
2	SNP/SQ/02/079-080	Construction of Road and Drain Works at Satkar Path of Ward No. 9	नगर स्तरीय	9	1,799,108.41	2079-07-22 (8 November, 2022)	श्री मोहम्मद गाजी निर्माण सेवा, सियारी-६	1,404,068.31	-21.96%	2079.09.19	2080.03.01	1,394,897.10	Complete
3	SNP/SQ/03/079-080	Construction of Drain Works (Siddhartha Path), Ward No. 3	शशर्त अनुदान (प्रदेश) र नगर स्तरीय	3	1,400,427.03	2079-08-15 (1 December, 2022)	श्री अन्जुली कन्स्ट्रक्सन, सि.न.पा.-६	1,132,286.14	-19.15%	2079.09.25	2080.01.18	996,293.39	Complete
4	SNP/SQ/04/079-080	Construction and Upgrading of Janta Path East-South Side (Siddhartha Path), Ward No. 12	नगर स्तरीय	12	1,699,942.78	2079-08-29 (15 December, 2022)	श्री वाराही निर्माण सेवा, सि.न.पा.	1,272,960.79	-25.12%	2079.10.09	2080.01.21	1,220,240.68	Complete
5	SNP/SQ/05/079-080	Construction of Sanskrit School Sabha Hall of Ward No. 03	शशर्त अनुदान (प्रदेश)	3	1,499,571.55	2079-09-18 (2nd January 2023)	श्री अन्जुली कन्स्ट्रक्सन, सि.न.पा.-६	1,309,027.74	-12.71%	2079.11.28	2080.02.30	982,268.25	Running
6	SNP/SQ/06/079-080	Construction of Building Construction (Finishing) Work, (Package 02) at Ward No. 1	विशेष अनुदान (प्रदेश)	1	1,999,971.98	2079-10-13 (26 January 2023)	श्री बेला निर्माण सेवा, सि.न.पा.-६	1,949,447.09	-2.53%	2079.11.22	2080.03.15	1,915,212.52	Complete

14

३) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को दरभाउपत्रको (Sealed Quotation- SQ) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
7	SNP/SQ/07/079-080	Drain and Road Construction & Road Upgrading Work, Ward No. 1	शशर्त अनुदान (प्रदेश)	1	1,600,000.00	2079-10-23 (6 February 2023)	श्री सफिक निर्माण सेवा, सि.न.पा.-११	1,240,749.00	-22.45%	2079.11.30	2080.03.15	1,205,185.99	Complete
8	SNP/SQ/08/079-080	Construction of Road and Drain works at Thapa Path and Mama Bhanji Path at Ward No. 9	नगर स्तरीय	9	1,599,236.68	2079-11-05 (17 February 2023)	श्री शितला निर्माण सेवा प्रा.लि., सि.न.पा.-९	1,209,148.00	-24.39%	2079.12.14	2080.03.05	1,206,221.15	Complete
9	SNP/SQ/09/079-080	Construction and Upgrading of Bhairahawa Taekwondo club Hall at Ward No. 3	नगर स्तरीय	3	1,913,702.97	2079-11-05 (17 February 2023)	श्री राज कन्स्ट्रक्सन, सि.न.पा.-८	1,657,377.00	-13.39%	2079.12.12	2080.03.05	1,562,234.13	Complete
10	SNP/SQ/10/079-080	Drain Construction work at Ward No. 9, Ward office to East side road	नगर स्तरीय	9	1,999,958.26	2079-11-12 (24 February 2023)	श्री शितला निर्माण सेवा प्रा.लि., सि.न.पा.-९	1,940,431.00	-2.98%	2079.12.13	2080.03.15	1,720,138.43	Complete
11	SNP/SQ/11/079-080	Construction of Breast Feeding Room at Ward No. 10	नगर स्तरीय	10	1,999,754.14	2079-11-29 (13 March 2023)	श्री अहमद निर्माण सेवा, सि.न.पा.-९	1,565,842.68	-21.70%	2079.12.30	2080.03.15	1,399,682.07	Complete
12	SNP/SQ/12/079-080	Upgrading of Krishna Path at Si.Na.Pa. 8	नगर स्तरीय	8	1,099,756.44	2079-11-29 (13 March 2023)	श्री बेला निर्माण सेवा, सि.न.पा.-६	840,906.16	-23.54%	2080.01.05	2080.03.15	810,201.78	Complete
												15	

३) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को दरभाउपत्रको (Sealed Quotation- SQ) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
13	SNP/SQ/13/079-080	Breast Feeding Room Construction Work, Siddharthanagar-1	नगर स्तरीय	1	1,831,815.70	2079-12-06 (20 March 2023)	श्री आरफा कन्स्ट्रक्सन प्रा.लि., काठमाडौं-३१	1,287,859.02	-29.69%	2080.01.11	2080.03.15	1,169,576.84	Complete
14	SNP/SQ/14/079-080	Construction of R.C.C. Drain at Shree Krishna Path, Ward No. 12	नगर स्तरीय अन्य पूँजीगत र क्रमागत योजना	12	1,600,613.65	2079-12-14 (28 March 2023)	श्री बेला निर्माण सेवा, सि.न.पा.-६	1,184,871.26	-25.97%	2080.01.14	2080.03.06	1,132,988.08	Complete
15	SNP/SQ-15/079-080	Drain Cover Slab Construction Work at Narayan Path, Maitri Path, Bank Road, South side of Traffic Office Drain & Other road Rupandehi.	नगर स्तरीय	all	2,000,000.00	2079-12-15 (29 March 2023)	श्री बेला निर्माण सेवा, सि.न.पा.-६	1,948,596.42	-2.57%	2080.01.14	2080.03.15	1,370,680.96	Running
16	SNP/SQ-16/079-080	Road Construction Work at Piprahiya Road to RP Chaudhari House Road at Ward No. 06	नगर स्तरीय अन्य पूँजीगत	6	1,532,497.16	2079-12-15 (29 March 2023)	श्री राजेश निर्माण सेवा, सि.न.पा.-६	1,492,853.92	-2.59%	2080.01.13	2080.03.15	1,431,468.48	Complete
17	SNP/SQ-17/079-080	Drain and Road Construction Work at Sukra Path	नगर स्तरीय अन्य पूँजीगत	3	1,999,847.69	2079-12-15 (29 March 2023)	श्री अनुराधा कन्स्ट्रक्सन, सि.न.पा.-९	1,957,132.65	-2.14%	2080.01.11	2080.03.15	1,900,930.18	Complete
18	SNP/SQ-18/079-080	Road upgrading & Maintenance Construction work at Ward-8, Danda Tole Madarsha Road Near Mayadevi Gumba	नगर स्तरीय अन्य पूँजीगत	8	1,527,892.31	2079-12-15 (29 March 2023)	श्री जि.एस.पि. ईन्जिनियर्स एण्ड विल्डर्स प्रा.लि., काठमाडौं-१०	1,115,732.50	-26.98%	2080.01.17	2080.03.15	1,102,993.20	Complete
												16	

३) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को दरभाउपत्रको (Sealed Quotation- SQ) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
19	SNP/SQ-19//079-080	Drain & Road Construction Work at ward-8, Sai Global School to west Road	नगर स्तरीय अन्य पूँजीगत	8	1,999,184.00	2079-12-15 (29 March 2023)	श्री जि.एस.पि. इन्जिनियर्स एण्ड बिल्डर्स प्रा.लि., काठमाडौं-१०	1,485,914.60	-25.67%	2080.01.17	2080.03.15	1,450,273.67	Complete
20	SNP/SQ-20//079-080	Drain & Road Construction Work at Ward-7 & 9, Himani path to north, Ward Connect Road	नगर स्तरीय अन्य पूँजीगत	7, 9	1,993,405.28	2079-12-15 (29 March 2023)	श्री जि.एस.पि. इन्जिनियर्स एण्ड बिल्डर्स प्रा.लि., काठमाडौं-१०	1,597,872.45	-19.84%	2080.01.17	2080.03.15	1,583,504.88	Complete
21	SNP/SQ-21//079-080	Road Construction Work at Udaypur and Road & Drain Construction at Khushi Path	क्रमागत योजना	9	1,957,571.82	2079-12-24 (7 April 2023)	श्री बेलाल निर्माण सेवा, सि.न.पा.-६	1,605,499.62	-17.99%	2080.02.03	2080.03.16	1,486,684.22	Complete
22	SNP/SQ-22//079-080	Construction of Boundary Wall Ward No. 12, Bhairahawa Multiple Campus	शशर्त अनुदान (प्रदेश)	12	1,499,961.30	2080-01-04 (17 April 2023)	श्री लक्की एण्ड शिव कन्स्ट्रक्सन, काठमाडौं-१२	1,131,753.19	-24.55%	2080.01.27	2080.03.15	1,045,696.44	Complete
23	SNP/SQ-23//079-080	Road & Drain Construction Work, Siddharthanagar Municipality-1, Harnaiya, Ward No. 8, Kawarsthan Road, Danda Gaown Rupandehi	नगर स्तरीय अन्य पूँजीगत	1,8	1,999,508.37	2080-01-05 (18 April 2023)	श्री वैष्णवी निर्माण सेवा, बगाहा-२	1,561,213.75	-21.92%	2080.02.02	2080.03.15	1,539,489.76	Complete
17													

३) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. को दरभाउपत्रको (Sealed Quotation- SQ) विवरण (निर्माण सम्बन्धि)													
S. N.	Contract Identification No.	Description of work	Source of Budget	Ward No.	Estimated Amount (with PS, VAT & Contingencies)	Bid Publication Date	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	% below	Agreement Date	Work Completion Date	Total Amount Payment	Remarks
24	SNP/SQ-24//079-080	Floor Construction Work (Ran Gaown Eidgah) Siddharthanagar Municipality-1, Rani Gaown, Rupandehi	नगर स्तरीय अन्य पूँजीगत	1	1,721,235.53	2080-01-05 (18 April 2023)	श्री बेलाल निर्माण सेवा, सि.न.पा.-६	1,036,572.46	-39.78%	2080.02.03	2080.03.16	1,022,578.49	Complete
					42,074,696.04			34307667.75	-18.46%			31,947,650.18	

कुल लागत = ४,२०,७४,६९६.०४

कुल ठेक्का कबोल रकम = ३,४३,०७,६६७.७५

कुल ठेक्का घटी % = १८.४६ %

४) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. मा राष्ट्रिय बोलपत्र मार्फत भएका कामहरु मध्ये केहि मुख्य मुख्य कामहरु (निर्माण सम्बन्धि)							
सि.न.	ठेक्का न.	ठेक्काको नाम	निर्माण व्यवसायीको नाम	ठेक्काको हालको अवस्था	प्रगति (भौतिक र वित्तीय)	जरिवाना	ठेक्कामा हुने निर्माणको विवरण
1	NCB/SNP/02/079-080 (e-bid)	Construction and Upgrading of Road and Drain works at West side Darkhasuwa passing through Siddhartha Yatayat Samiti, Ward no. -03	श्री वैष्णवी निर्माण सेवा, बगाहा-२	Complete	भौतिक (%) : ९०.७९ वित्तीय (%) : ८९.८७	-	210m Brick Masonary Drain both sides and 112m Brick Masonary Drain single side and gravel with grading and rolling
2	NCB/SNP/03/079-080	Construction of Road, Drain and other structures including building maintainance and plumbing on different locations of Ward no. 12	श्री अहमद निर्माण सेवा, सि.न.पा.-९	Complete	भौतिक (%) : ९७.१३ वित्तीय (%) : ९५.२९	-	Uday Path West Road Towards Bijay Gurungs House, Bhrikuti Path, Siddhartha Path, Friends Colony, Jay Buddha Path, Kalika Colony, Dipjyoti Path
3	SNP/NCB-07/079-080	Construction of Road and Drain Work at ward 7	श्री शितला निर्माण सेवा, सि.न.पा.-९	Complete	भौतिक (%) : ९९.२२ वित्तीय (%) : ९८.०३	-	140m RCC Drain both sides and gravel.
4	SNP/NCB-08/079/080	Fulpur Culvert, Fulpur Remain Road and Drain work, Jhandi Bazar to dadagaun at ward No. 2, Siddharthanagar Municipality	श्री क्रान्ति निर्माण सेवा, सि.न.पा.-२	Complete	भौतिक (%) : १०२.५७ वित्तीय (%) : ९९.८८	-	fulpur culvert, fulpur remaining road and drain work, jhandi bazaar to dada gaun road
5	SNP/NCB-12/079/080	Construction of Road, Drain and other Structures on Different Locations of ward no. 13,	श्री मोहम्मद गाजी निर्माण सेवा, सियारी-४	Complete	भौतिक (%) : ९०.६६ वित्तीय (%) : ९०.९४	-	Binayak Path, Radha Krishna Path, Shradha Path West Galli, Shantinagar - west galli of susanskrit school Road, Surya Path East Galli road towards Manoj Guptas House, Road Towards Chandra Prakash Shrestha's House.
6	SNP/NCB-13/079/080	Construction of Road, Drain and other Structures on Different Locations of ward no. 03	श्री मनिष निर्माण सेवा, सि.न.पा.-८	Complete	भौतिक (%) : ९०.६८ वित्तीय (%) : ९०.९७	१,३७,०९,४०९ (७९ दिन, प्रतेक दिन १९३०।०९)	Mahamaya Path Ramu Bhandari house to West Side , Buddha Santi Path South to north east Sita K.C. house, Pancharatna Tole Harish Chettri house side

४) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. मा राष्ट्रिय बोलपत्र मार्फत भएका कामहरु मध्ये केहि मुख्य मुख्य कामहरु (निर्माण सम्बन्धि)							
सि.न.	ठेक्का न.	ठेक्काको नाम	निर्माण व्यवसायीको नाम	ठेक्काको हालको अवस्था	प्रगति (भौतिक र वित्तीय)	जरिवाना	ठेक्कामा हुने निर्माणको विवरण
7	SNP/NCB-14/079/080 (e-bid)	Construction of Shree Nawadurga Secondary School Building at SNP Ward no. -04	श्री जगरनाथ निर्माण व्यवसाय, तिलोत्तमा-५	Complete	भौतिक (%) : १००.२९ वित्तीय (%) : ९९.३२	-	Two Storied School Building
8	SNP/NCB-15/079/080	Ward Office Building Construction Work at Siddharthanagar Municipality, Ward no. 7	श्री अहमद निर्माण सेवा, सि.न.पा.-९	Complete	भौतिक (%) : ९६.४४ वित्तीय (%) : ९६.८८	-	Additional One Storied on Existing Ward Office - 07 Building
9	SNP/NCB-18/079/080	Construction of Ward Office Building Works, Ward No. 2	श्री क्रान्ति निर्माण सेवा, सि.न.पा.-२	Complete	भौतिक (%) : ९२.४३ वित्तीय (%) : ९०.३६	-	Additional one storied RCC building and Additional Truss on Roof on existing Building of Ward Office - 02 Building
10	SNP/NCB-19/079/080	Construction of Guard House Building and Remaining Boundary wall at Panch Batika (Prithivi Park), Ward No. 2	श्री क्रान्ति निर्माण सेवा, सि.न.पा.-२	Complete	भौतिक (%) : ९७.९० वित्तीय (%) : ९४.५२	-	Single Storied Guard House Building and Boundary Protection Works.
11	SNP/NCB-21/079/080 (e-bid)	Construction of Guard Room, Drain, Footpath and Upgrading Compound wall and Landscaping at Darkhasuwa Park, Ward No. 3	श्री बागेश्वरी निर्माण सेवा, सि.न.पा.-१०	Complete	भौतिक (%) : ९०.९३ वित्तीय (%) : ९१.९३	-	109m RCC Drain, Compound Wall, Footpath,Transported Soil, Grading, Rolling, Electric Pole, Steps on Toilet and Sheds, Ticket Counter
12	SNP/NCB-22/079/080	Construction and upgrading of Road, Drain and other structures on different locations of Ward No. 11	श्री सफिक निर्माण सेवा, सि.न.पा.-११	Complete	भौतिक (%) : ९१.८८ वित्तीय (%) : ८८.३७	-	Siswa Gaau North to Madarna school and towards Gauram Buddha International Airport , Bhujauli Gaau to South-west (Naresh Ghai ghar to Badera Tree), Siswa Gaau to Ghagara Khola Road

४) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. मा राष्ट्रिय बोलपत्र मार्फत भएका कामहरु मध्ये केहि मुख्य मुख्य कामहरु (निर्माण सम्बन्धि)							
सि.न.	ठेक्का न.	ठेक्काको नाम	निर्माण व्यवसायीको नाम	ठेक्काको हालको अवस्था	प्रगति (भौतिक र वित्तीय)	जरिवाना	ठेक्कामा हुने निर्माणको विवरण
13	SNP/NCB-26/079/080	Construction of Khajana Basic School, Ward No. 3	श्री प्रितम विल्डर्स, सि.न.पा.-४	Complete	भौतिक (%) : ९८.५४ वित्तीय (%) : ९८.३७	-	Top Storey Finishing Works and dismantalling of Existing Old Structures.
14	SNP/NCB-30/079/080	Construction of Road, Drain and other structures on different locations of Ward No. 4	श्री सौरभ विल्डर्स, सि.न.पा.-६	Running	भौतिक (%) : ५२.११ वित्तीय (%) : ५२.४२	-	Samai maai Mandir, Hardis Path, Gumba of Airport, Lautan Path, Lumbini Road towards Ward office-4 through Gumba, Bhawani Path
15	SNP/NCB-31/079/080 (e-bid)	Building Construction Work of Bahira Baal Ma. Bi. Ward No. 2	श्री वैष्णवी निर्माण सेवा, बगाहा-२	Complete	भौतिक (%) : ९५.२४ वित्तीय (%) : ९४.९९	-	One Storied Building
16	SNP/NCB-33/079/080	Drain and RCC Road Construction Work, Siddharthanagar Municipality-7, Vijaya Path & Ramjanaki Path, Rupandehi	श्री शितला निर्माण सेवा, सि.न.पा.-९	Complete	भौतिक (%) : ९९.८८ वित्तीय (%) : ९९.९२	-	Vijaya Path & Ramjanaki Path
17	SNP/NCB-34/079/080	Construction of Boundary wall at Shree Nawadurga Secondary School, Ward No. 4	श्री भिमगंगा निर्माण सेवा, सि.न.पा.-८	Complete	भौतिक (%) : ९९.४० वित्तीय (%) : ९९.२४	-	Boundary Wall and Gate
18	SNP/NCB-35/079/080	Construction of Road, Drain and other structures on different locations of Ward No. 11	श्री पाल कन्स्ट्रक्सन, काठमाडौं-१०	Complete	भौतिक (%) : ९७.०० वित्तीय (%) : ९८.१६	-	Piparahiya to shankarpur, Naudihawa road.(Starting from Boarder) 21

४) सिद्धार्थनगर नगरपालिका २०७९।८० आ.व. मा राष्ट्रिय बोलपत्र मार्फत भएका कामहरु मध्ये केहि मुख्य मुख्य कामहरु (निर्माण सम्बन्धि)							
सि.न.	ठेक्का न.	ठेक्काको नाम	निर्माण व्यवसायीको नाम	ठेक्काको हालको अवस्था	प्रगति (भौतिक र वित्तीय)	जरिवाना	ठेक्कामा हुने निर्माणको विवरण
19	SNP/NCB-40/079/080 (e-bid)	Construction of Garage for Tractors and other vehicles of Siddharthanagar Municipality at Bus Park of Ward No. 3	श्री अनुराधा कन्स्ट्रक्सन, सि.न.पा.-९	Complete	भौतिक (%) : ९२.९२ वित्तीय (%) : ९४.२४	-	Garage Construction of Capacity 17 Tractor.
20	SNP/NCB-42/079/080	Construction of Drain, Drain Cover & RCC Road Construction Work at Siddharthanagar Municipality, Ward No. 7	श्री कोटहीमाई कन्जहियामाई कन्स्ट्रक्सन	Complete	भौतिक (%) : ९३.१६ वित्तीय (%) : ९१.८१	-	Laigurash Path, Kailash path, Deurali path To West, South Side of Ward Office

५) सिद्धार्थनगर नगरपालिकाबाट संचालित बहुवर्षिय योजना							
कार्यालयको नाम : सिद्धार्थनगर नगरपालिका							
ठेक्का नं. र निर्माण कार्यको विवरण	निर्माण व्यवसायीको नाम	Bid Amount (with VAT & PS)	सम्झौता मिति	शुरू सम्झौता बमोजिम कार्य सम्पन्न गर्नु पर्ने मिति	म्याद थप पश्चात कार्य सम्पन्न गर्नु पर्ने मिति	प्रगति (भौतिक र वित्तीय)	ठेक्काको हालको अवस्था
Admin_Building_Siddhartha_Mun_NCB_MB_077_078, Administrative Building Construction of Siddharthanagar Municipality, Ward No. 5, Siddharthanagar Municipality, Rupandehi	M/S Sky/Ramsagar J.V., Kathmandu	18,37,49,537.5	2078-03-24	2080-06-17	-	भौतिक (%) : ५६.२५ वित्तीय (%) : ६०.७३ as per measurement on 2080/01/10	Running
CAMIDW_HATB_SOUTH_NCB_01B, Community Agriculture Market Infrastructure Development Work, Hat Bazar, Siddharthanagar Municipality -13, Rupandehi.	M/S Bikash Brother/Aatreya/Basnet J.V., Sinamangal, Kathmandu.	16,38,17,260.51	2077-08-09	2079-03-16	2080/3/20 (without Liquidated Damage) 2080/09/29 (with Liquidated Damage)	भौतिक (%) : ३७.४५ वित्तीय (%) : ३९.७७ as per measurement on 2079/02/05	Running
SNP/NCB-25/078/079, Construction of New Entry Gate Belhiya Nepal -India Border, Ward No.1, Belhiya, Siddharthanagar Municipality.	M/S Laxmi Nirman Sewal Siddharthanagar-13, Rupandehi	1,64,62,546.96	2078-12-30	2079-02-15	2079/12/30 (without Liquidated Damage) 2080/3/15 (without Liquidated Damage) 2080/09/29 (without Liquidated Damage)	भौतिक (%) : २६.९९ वित्तीय (%) : ३६.०३ as per measurement on 2080/03/20	Running

६) कार्यक्रम कार्यान्वयनमा देखिएका समस्याहरू

- वार्डबाट छनौट भएर आउने कतिपय योजनाहरू बिवादित हुनु
- पर्याप्त बजेटको अभाव ।
- साईट समयमा उपलब्ध गराउन नसकिनु
- अन्तरनिकाय समन्वयको अभाव ।

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction



During Construction

Contract Identification No.:- NCB/SNP/01/079-080 Description of work:- Building Construction Work, Shree Paklihawa Secondary School, Ward no. – 01,
बिशेष अनुदान (संघीय)

25

७) महत्वपूर्ण कार्यहरुको फोटोहरु



During Construction



During Construction


Contract Identification No.:- NCB/SNP/01/079-080 Description of work:- Building Construction Work, Shree Paklihawa Secondary School, Ward no. – 01,
बिशेष अनुदान (संघीय)

26


७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction

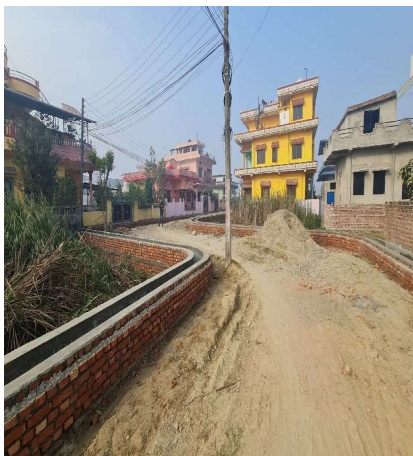

During Construction

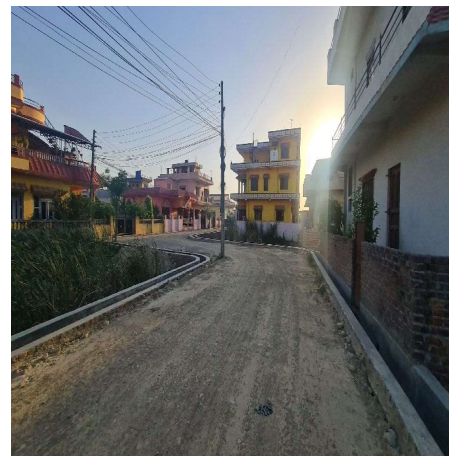


After Construction

Contract Identification No.:
NCB/SNP/02/079-080

Description of work:- Construction and Upgrading of Road and Drain works at West side Darkhasuwa passing through Siddhartha Yatayat Samiti, Ward no. – 03, नगर स्तरीय

27

७) महत्वपूर्ण कार्यहरुको फोटोहरु

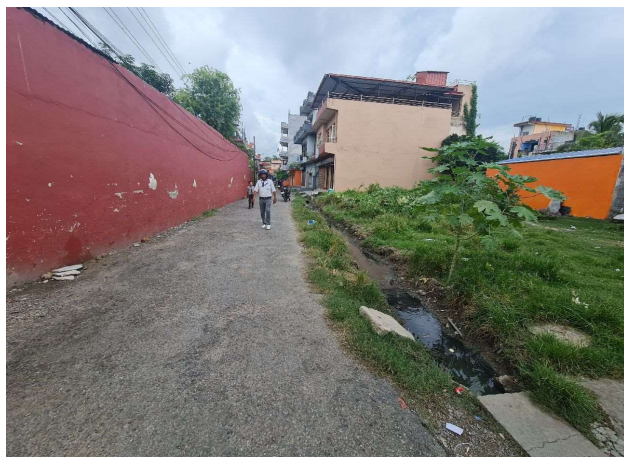

Before Construction, Kalika Colony



After Construction, Kalika Colony

Contract Identification No.:
NCB/SNP/03/079-080

Description of work:- Construction of Road, Drain and other structures including building maintainance and plumbing on different locations of Ward no. 12 , वडा स्तरीय

28

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction, Jay Buddha Path



After Construction, Jay Buddha Path

Contract Identification No.:-
NCB/SNP/03/079-080

Description of work:- Construction of Road, Drain and other structures including building maintainance and plumbing on different locations of Ward no. 12 , वडा स्तरीय

29

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction, Siddhartha Path north



After Construction, Siddhartha Path north

Contract Identification No.:-
NCB/SNP/03/079-080

Description of work:- Construction of Road, Drain and other structures including building maintainance and plumbing on different locations of Ward no. 12 , वडा स्तरीय

30

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction, Dipjyoti Path



After Construction, Dipjyoti Path

Contract Identification No.:-
NCB/SNP/03/079-080

Description of work:- Construction of Road, Drain and other structures including building maintainance and plumbing on different locations of Ward no. 12 , वडा स्तरीय

31

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction, Friends Colony



After Construction, Friends Colony

Contract Identification No.:-
NCB/SNP/03/079-080

Description of work:- Construction of Road, Drain and other structures including building maintainance and plumbing on different locations of Ward no. 12 , वडा स्तरीय

32

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction, Lekhnath Path




After Construction, Lekhnath Path


Contract Identification No.:- SNP/NCB-07/079-080 Description of work:- Construction of Road and Drain Work at ward 7 (Lekhnath Path & Trishul Path),
बडा स्तरीय र अन्य पूँजीगत

33

७) महत्वपूर्ण कार्यहरुको फोटोहरु

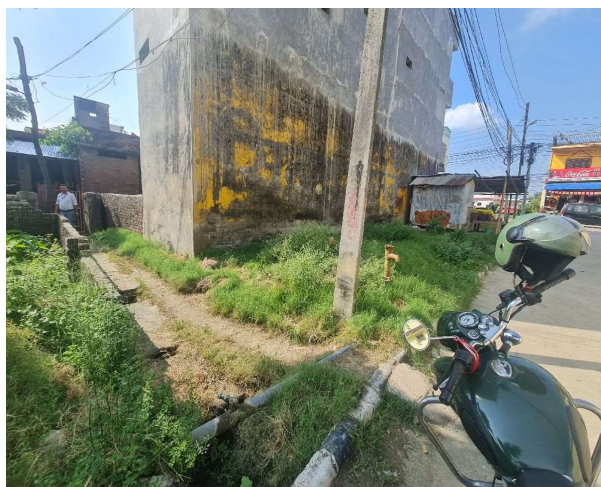

Before Construction, Shantinagar - west galli of susanskrit school Road.

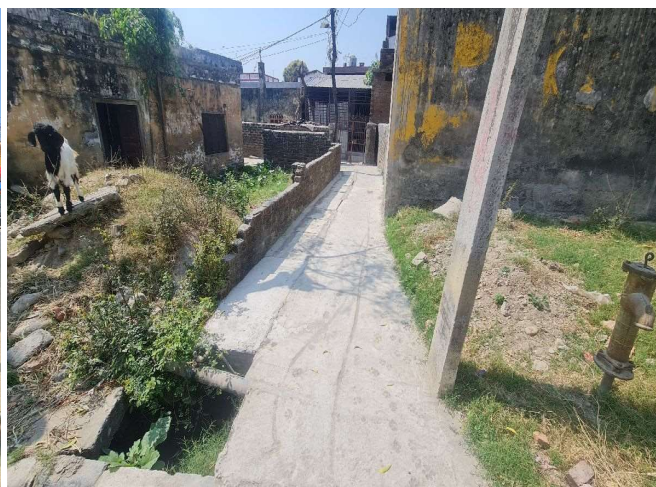


After Construction, Shantinagar - west galli of susanskrit school Road.

Contract Identification No.:- SNP/NCB-12/079/080 Description of work:- Construction of Road, Drain and other Structures on Different Locations of ward no. 13, बडा स्तरीय

34

७) महत्वपूर्ण कार्यहरुको फोटोहरु

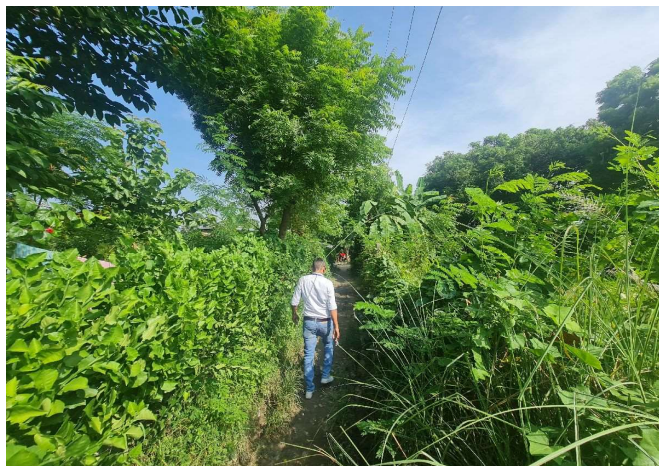

Before Construction, Surya Path East Galli road towards
Manoj Guptas House.




After Construction, Surya Path East Galli road towards
Manoj Guptas House.

Contract Identification No.:-
SNP/NCB-12/079/080

Description of work:- Construction of Road, Drain and other Structures on Different Locations of ward no.
13, बडा स्तरीय

35

७) महत्वपूर्ण कार्यहरुको फोटोहरु

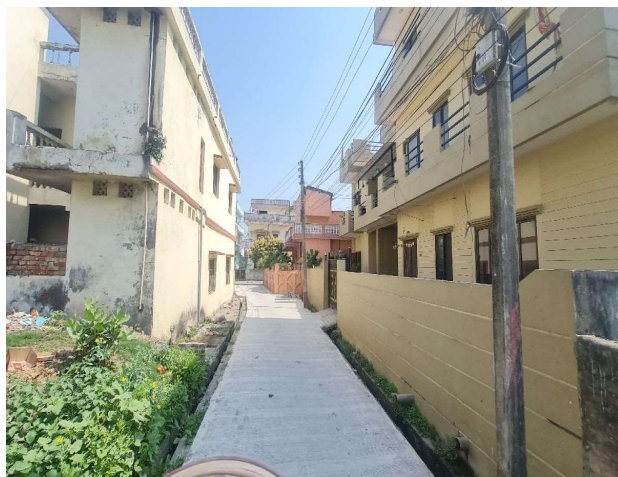

Before Construction, Binayak Path



After Construction, Binayak Path

Contract Identification No.:-
SNP/NCB-12/079/080


Description of work:- Construction of Road, Drain and other Structures on Different Locations of ward no.
13, बडा स्तरीय

36

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction, Radha Krishna Path

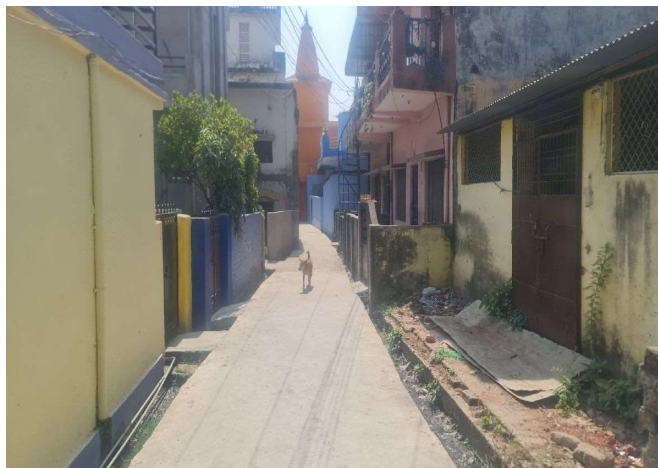

After Construction, Radha Krishna Path

Contract Identification No.:- SNP/NCB-12/079/080 Description of work:- Construction of Road, Drain and other Structures on Different Locations of ward no. 13, बडा स्तरीय

37

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction



During Construction



After Construction

Contract Identification No.:- SNP/NCB-14/079/080 Description of work:- Construction of Shree Nawadurga Secondary School Building at SNP Ward no. – 04, विशेष अनुदान (संघीय)

38

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Final Construction

Description of work:- Construction of Shree Nawadurga Secondary School Building at SNP Ward no. – 04, विशेष अनुदान (संघीय)

39

७) महत्वपूर्ण कार्यहरुको फोटोहरु



During Construction



After Construction

Contract Identification No.:-
SNP/NCB-31/079/080

Description of work:- Building Construction Work of Bahira Baal Ma. Bi. Ward No. 2 , शशर्त अनुदान (संघीय)
र अन्य पूँजीगत

40

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction



During Construction

Contract Identification No.:- Description of work:- Construction of Garage for Tractors and other vehicles of Siddharthanagar
 SNP/NCB-40/079/080 Municipality at Bus Park of Ward No. 3, नेपाल सरकार नगद अनुदान

41

७) महत्वपूर्ण कार्यहरुको फोटोहरु



After Construction

Contract Identification No.:- Description of work:- Construction of Garage for Tractors and other vehicles of Siddharthanagar
 SNP/NCB-40/079/080 Municipality at Bus Park of Ward No. 3, नेपाल सरकार नगद अनुदान

42

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction



During Construction

Contract Identification No.:- Description of work:- Chhath Pokhari Construction Work, Siddharthanagar-1, Naudihawa, अन्य पूँजीगत
SNP/NCB-52/079/080

43

७) महत्वपूर्ण कार्यहरुको फोटोहरु



After Construction

Contract Identification No.:- Description of work:- Chhath Pokhari Construction Work, Siddharthanagar-1, Naudihawa, अन्य पूँजीगत
SNP/NCB-52/079/080

44

७) महत्वपूर्ण कार्यहरुको फोटोहरु



Before Construction



During Construction

Contract Identification No.:- Description of work:- Construction of New Entry Gate Belhiya Nepal -India Boarder
SNP/NCB-25/078/079

45

७) महत्वपूर्ण कार्यहरुको फोटोहरु



During Construction

Contract Identification No.:- Description of work:- Construction of New Entry Gate Belhiya Nepal -India Boarder
SNP/NCB-25/078/079

46

द) अनुगमनका फोटोहरु



द) अनुगमनका फोटोहरु



द) अनुगमनका फोटोहरु



द) अनुगमनका फोटोहरु



८) अनुगमनका फोटोहरु



८) अनुगमनका फोटोहरु



८) अनुगमनका फोटोहरु



क्र. सं.	विषय क्षेत्र	उपक्षेत्र	ईकाइ	त्रैमासिक प्रगती - कुल
1	सडक	कालोपत्रे/ढलान	कि.मी.	९.६४४
		ग्रावेल	कि.मी.	८.६९७
		टयाक खोल्ने	कि.मी.	१.७
2	खानेपानी तथा सरसफाई	सार्वजनिक शौचालय	संख्या	६
3	सिँचाई	ढल निर्माण	कि.मी.	६.४५९६
4	जलविद्युत	टयुबेल जडान	वटा	११
5	फोहोरमैला व्यवस्थापन	प्रसारण लाइन	कि.मी.	०.२५
6	सार्वजनिक पूर्वाधार एवं भवन	डम्पिङ्ग साइट	संख्या	१
		विद्यालय भवन	संख्या	८
		स्वास्थ्य चौकी र स्वास्थ्य एकाइ	वटा	३
		आफ्नै स्वामित्वको सभागृह	वटा	१
		बसपार्क टर्मिनल	वटा	१
		सामुदायिक भवन	वटा	३
७	सार्वजनिक स्थल	पार्क निर्माण	वटा	१
		खेलकुद मैदान	वटा	१
		कभर्ड हल	वटा	१
८	पर्यटन पूर्वाधार	मनोरंजन पार्क	वटा	१
		पर्यटन स्थान/मन्दिर	वटा	२
९	वृक्षरोपण	जिर्णोद्धार गरिएका धार्मिक, स्मारक र पुरातत्व स्थल	वटा	३
९	वृक्षरोपण	वृक्षरोपण	संख्या	१०००



धन्यवाद !

55
